

Construction Metrics

Nora Embert

Senior Engineer II


Interconnection Construction
Management

May 2026 IPS


Generation Placed in Service (MWE)


	2022	2023	2024	2025	2026
Coal	-	-	-	29	-
Natural Gas	1,983	3,279	5	-	940
Nuclear	-	54	-	-	-
Other	-	-	-	-	-
Solar	1,074	1,301	4,451	2,713	847
Storage	-	61	43	20	16
Wind	0	282	286	255	13
Total	3,056	4,977	4,785	3,017	1,815

Status of Agreements by Year Signed

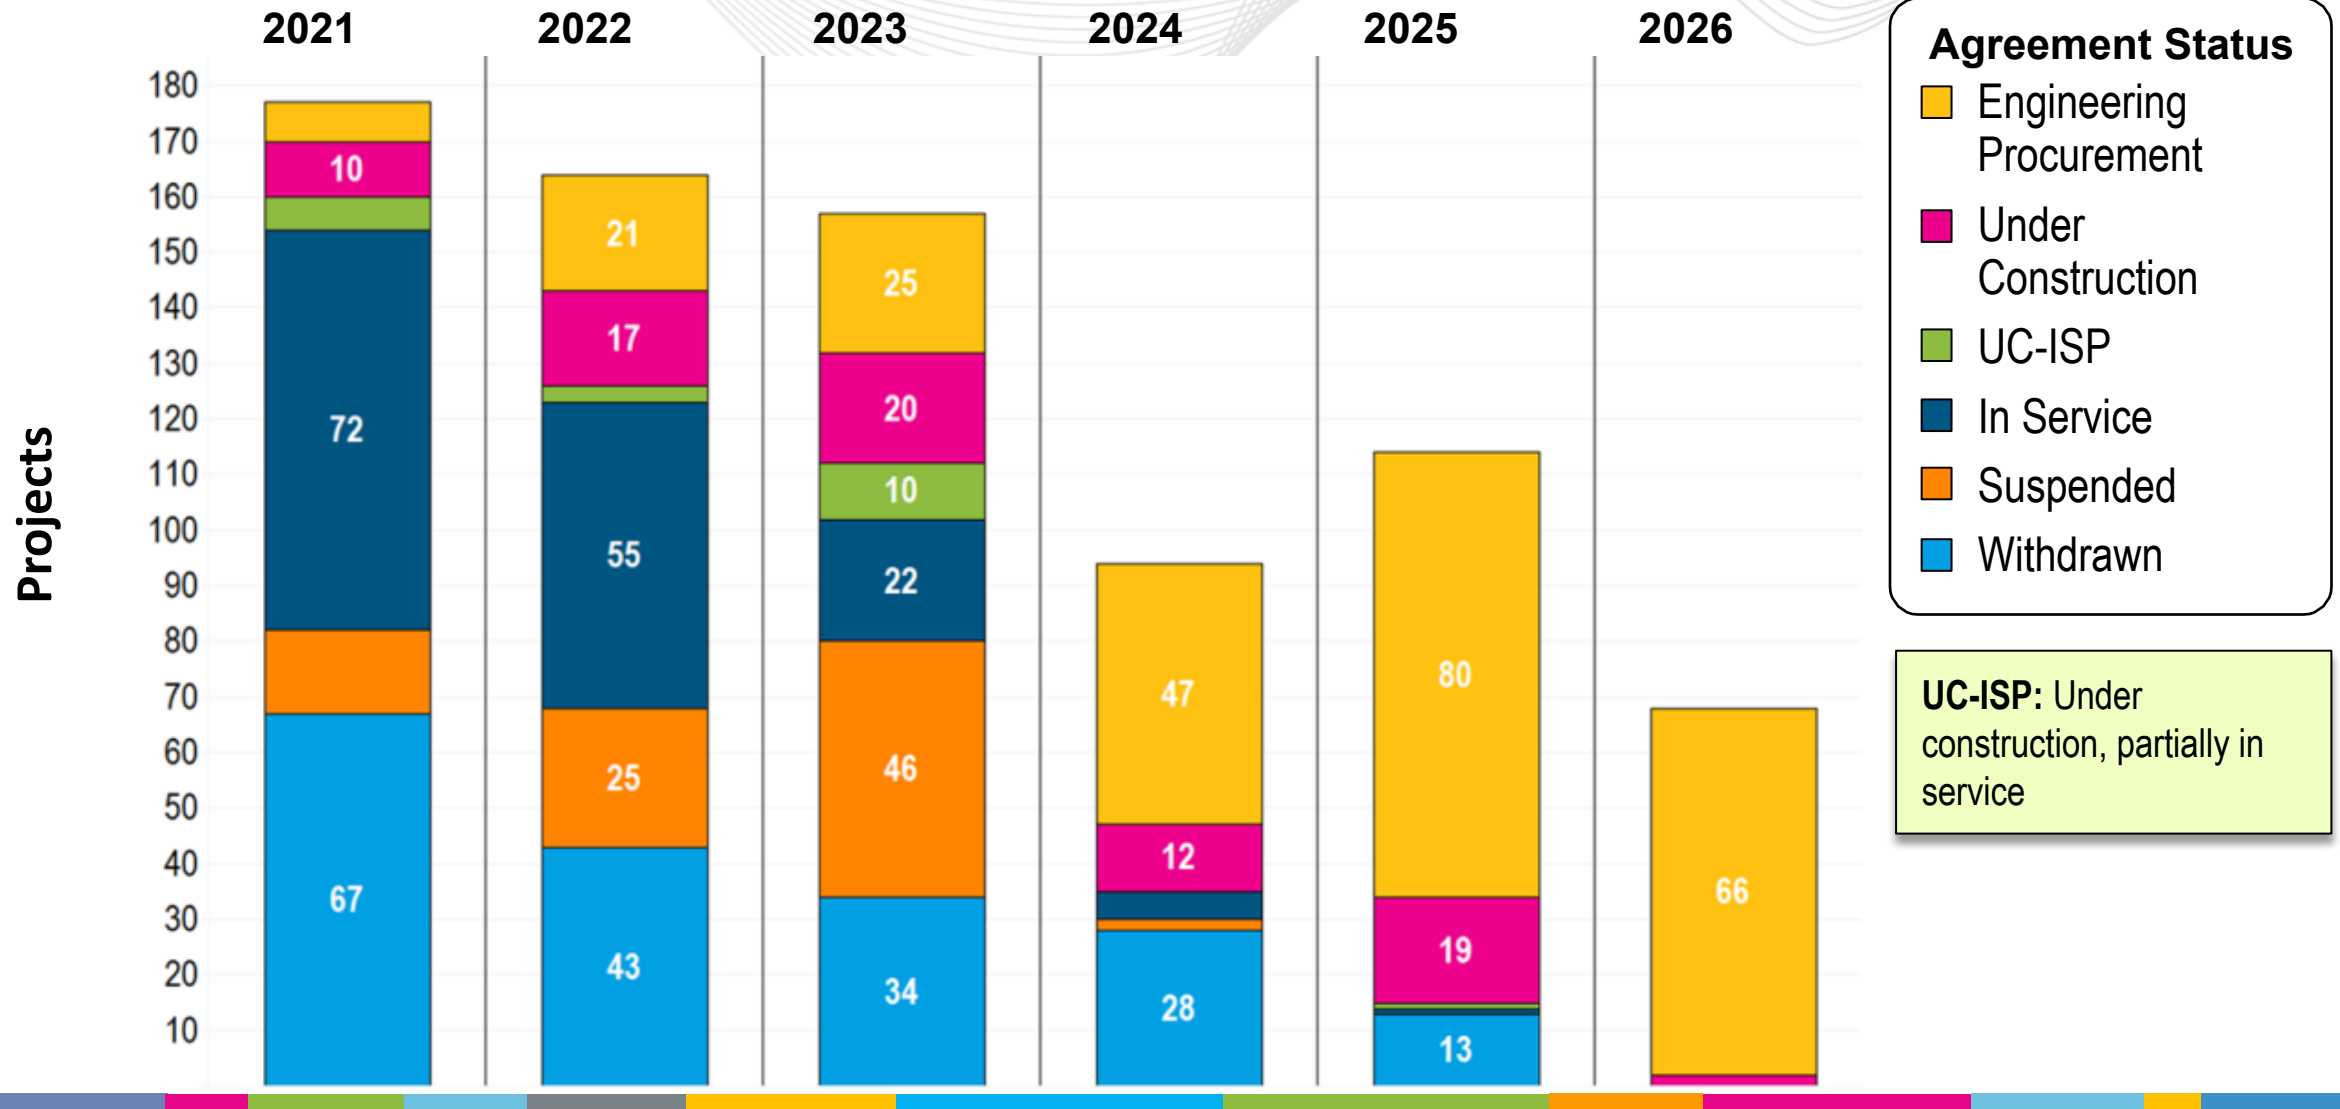


Status of Agreements by Year Signed

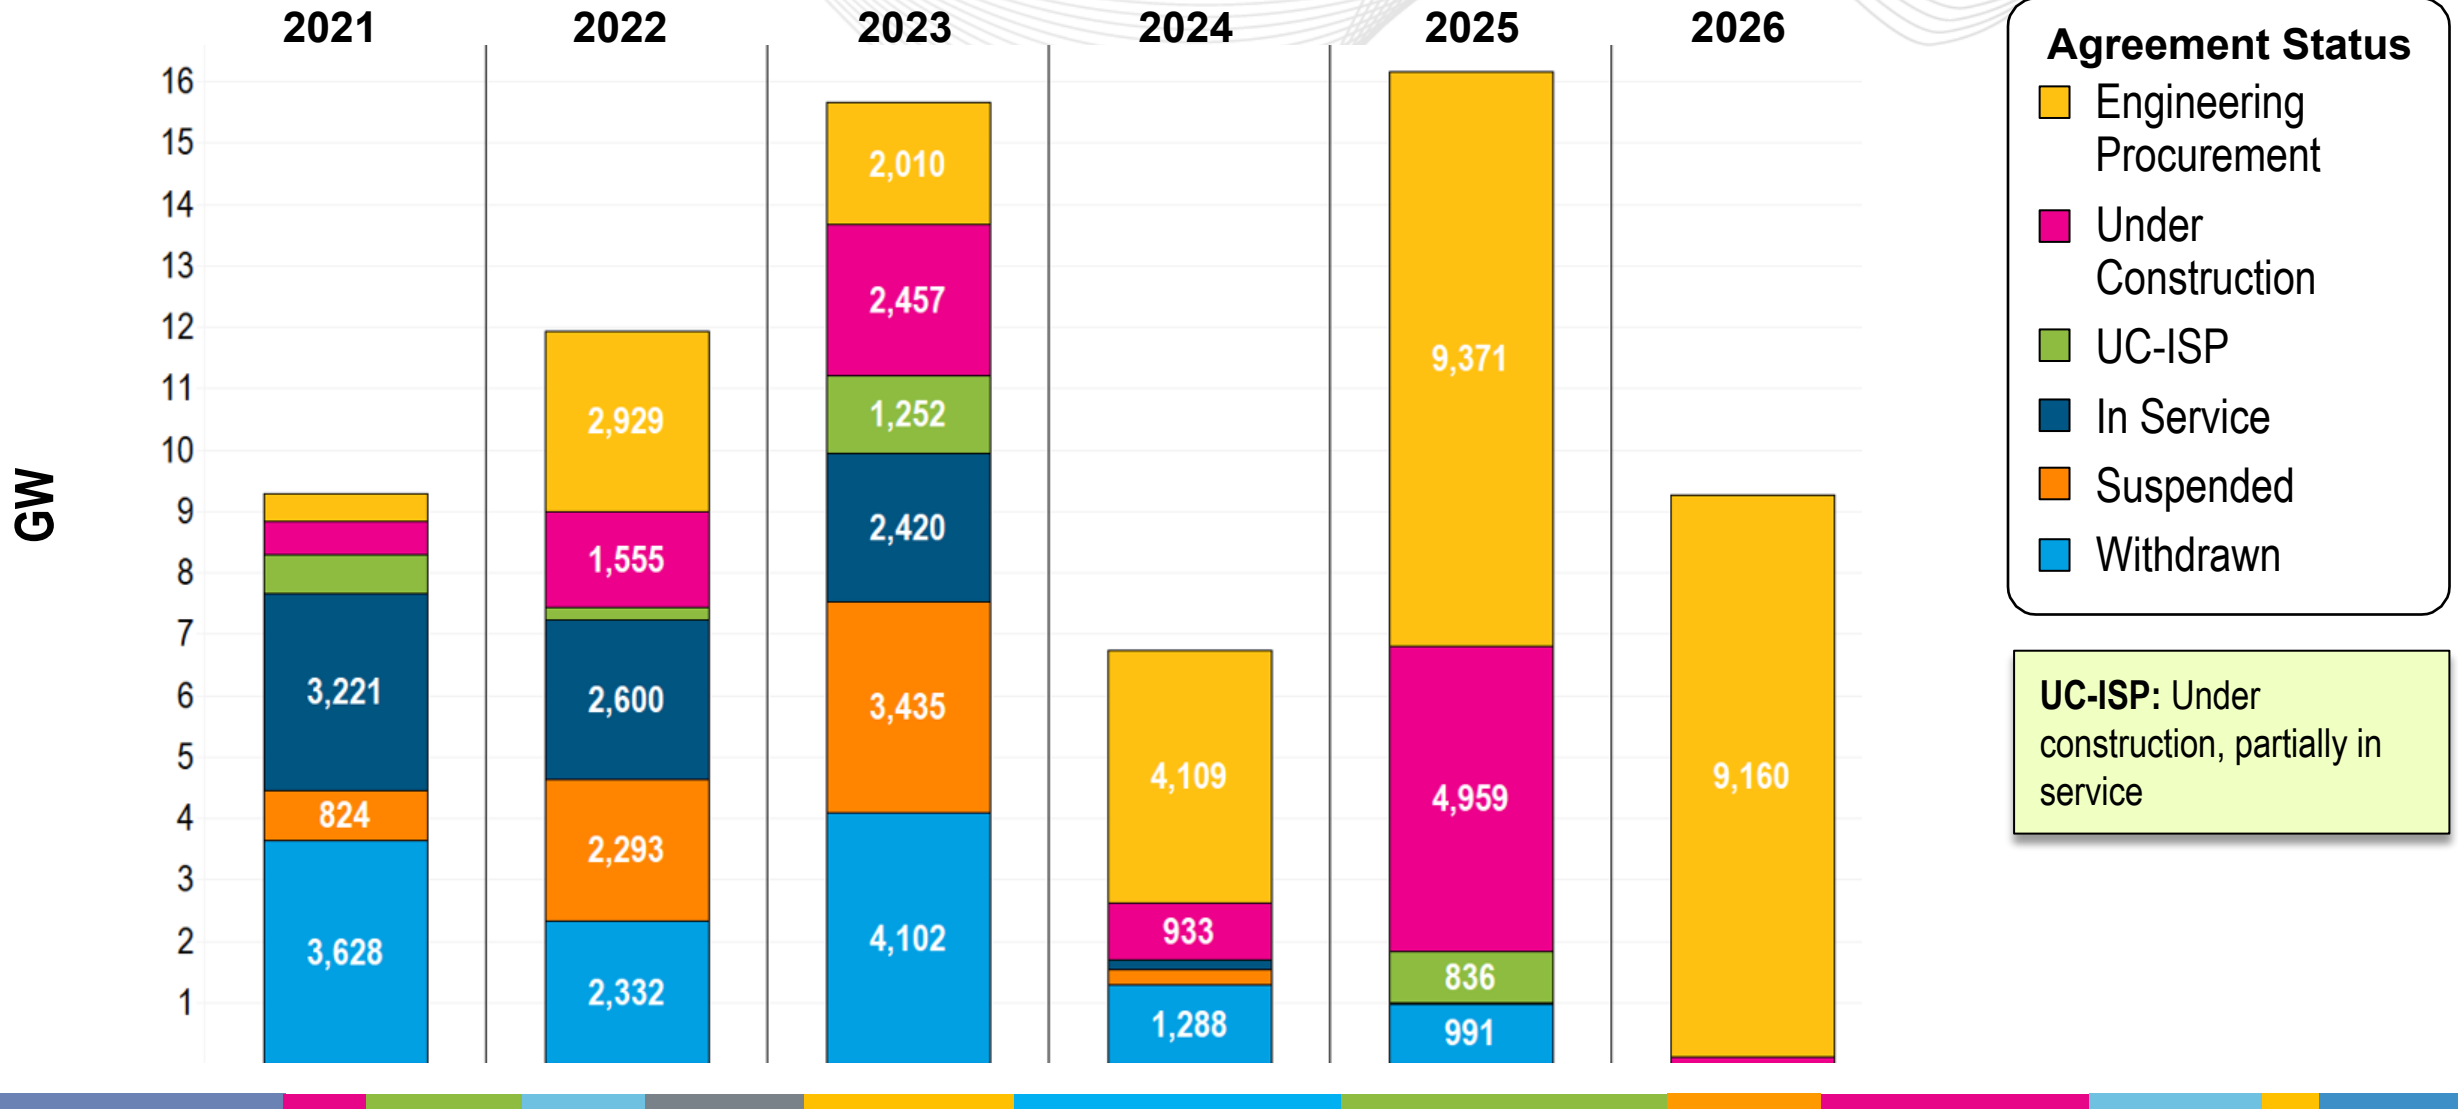


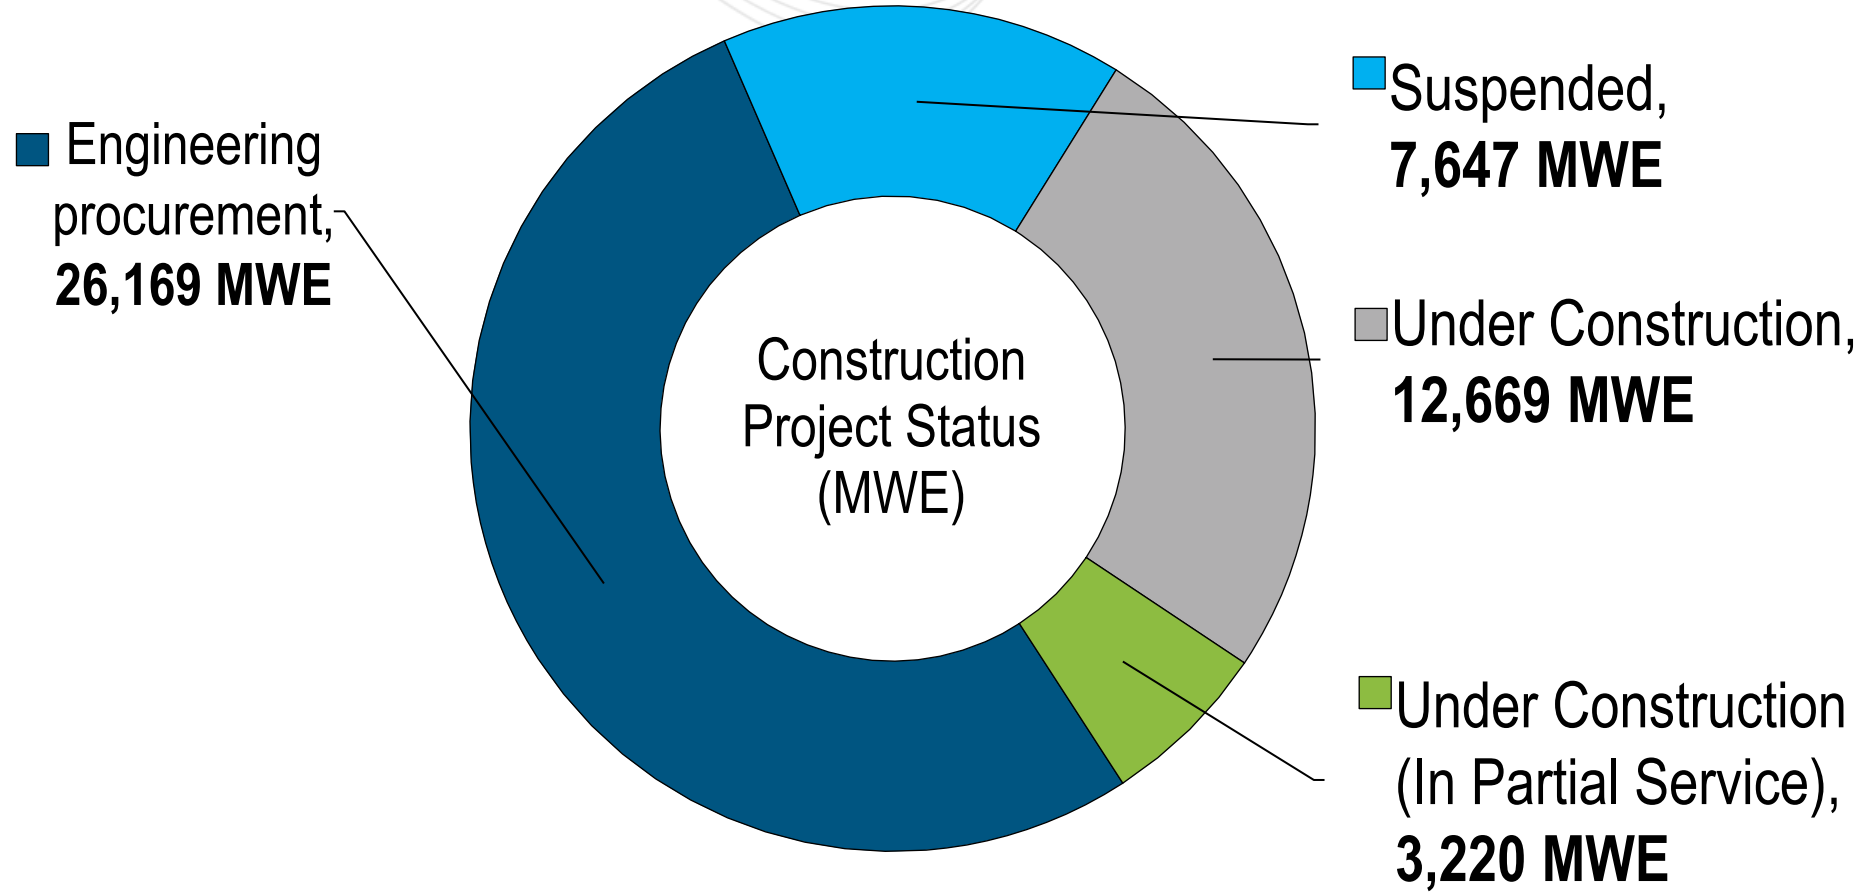


2025

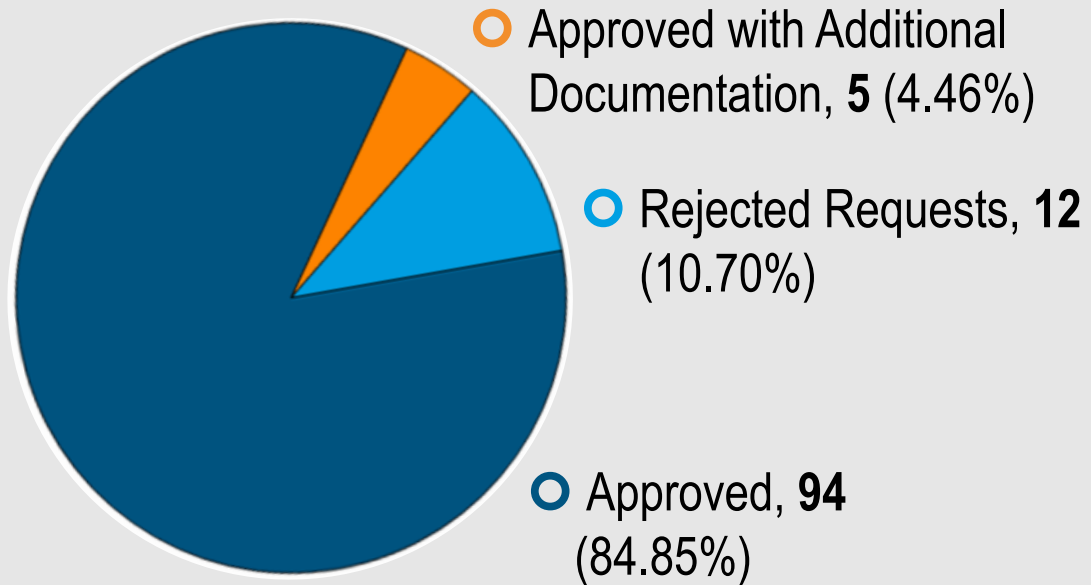


2026

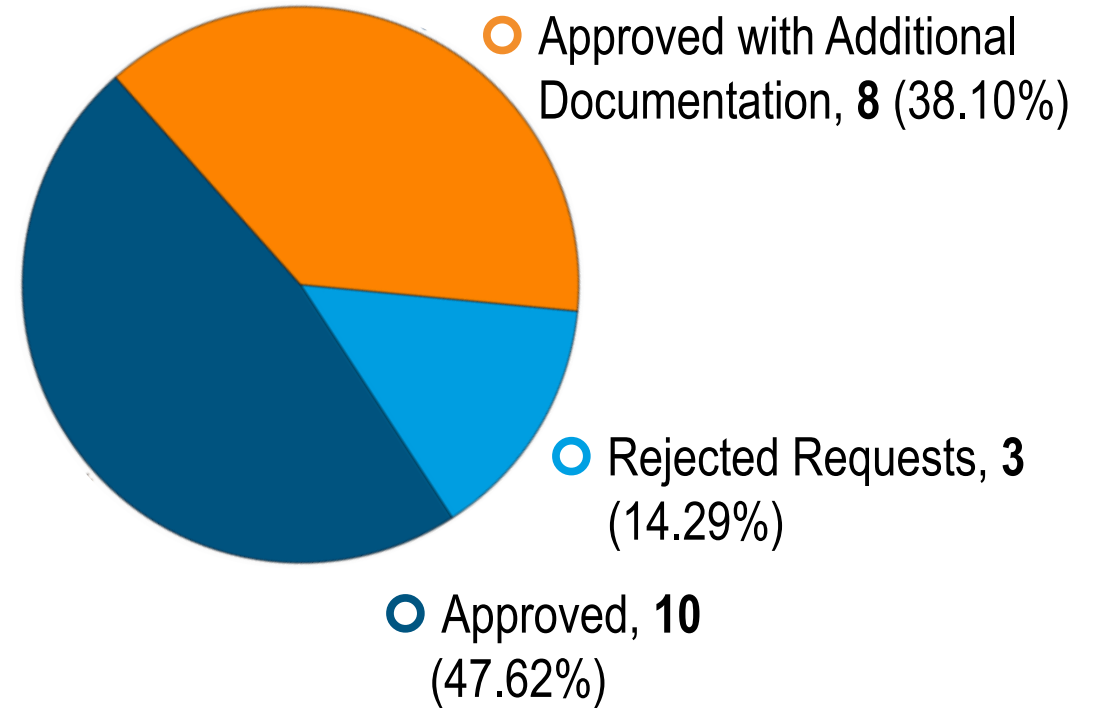

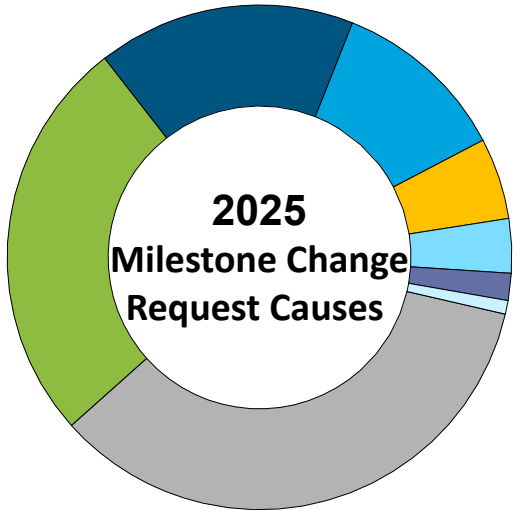


- Permitting Delays, 4000.00%,
- Equipment Delays, 3000.00%,
- Other, 1900.00%,
- TO Backfeed Move, 1300.00%,
- Equipment Challenges, 600.00%,
- TO Backfeed Move — Developer Delays,
- TO Construction Delays, 400.00%,
- TO Backfeed Move — Other, 100.00%,

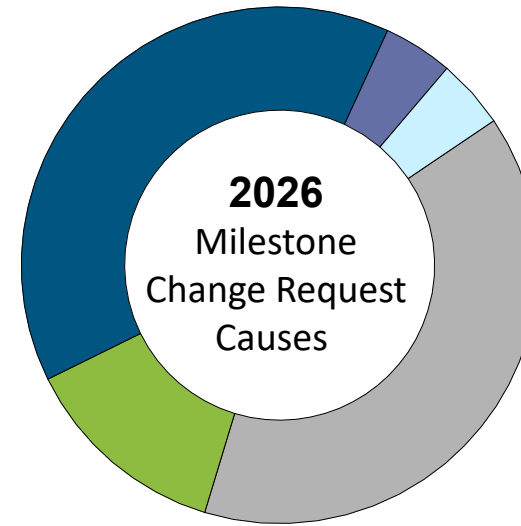


- Permitting Delays, 900.00%,
- Other, 900.00%,
- Equipment Delays, 300.00%,
- TO Backfeed Move — Developer Delays, 100.00%,
- TO Backfeed Move — Other, 100.00%,


○ **Other:** includes various delay such as land ownership, ownership transfer, Engineering Procurement and Construction Contractor (EPC) procurement, equipment issues, and construction delays


TO Backfeed Move: The date by which the Transmission owner can provide backfeed has shifted.

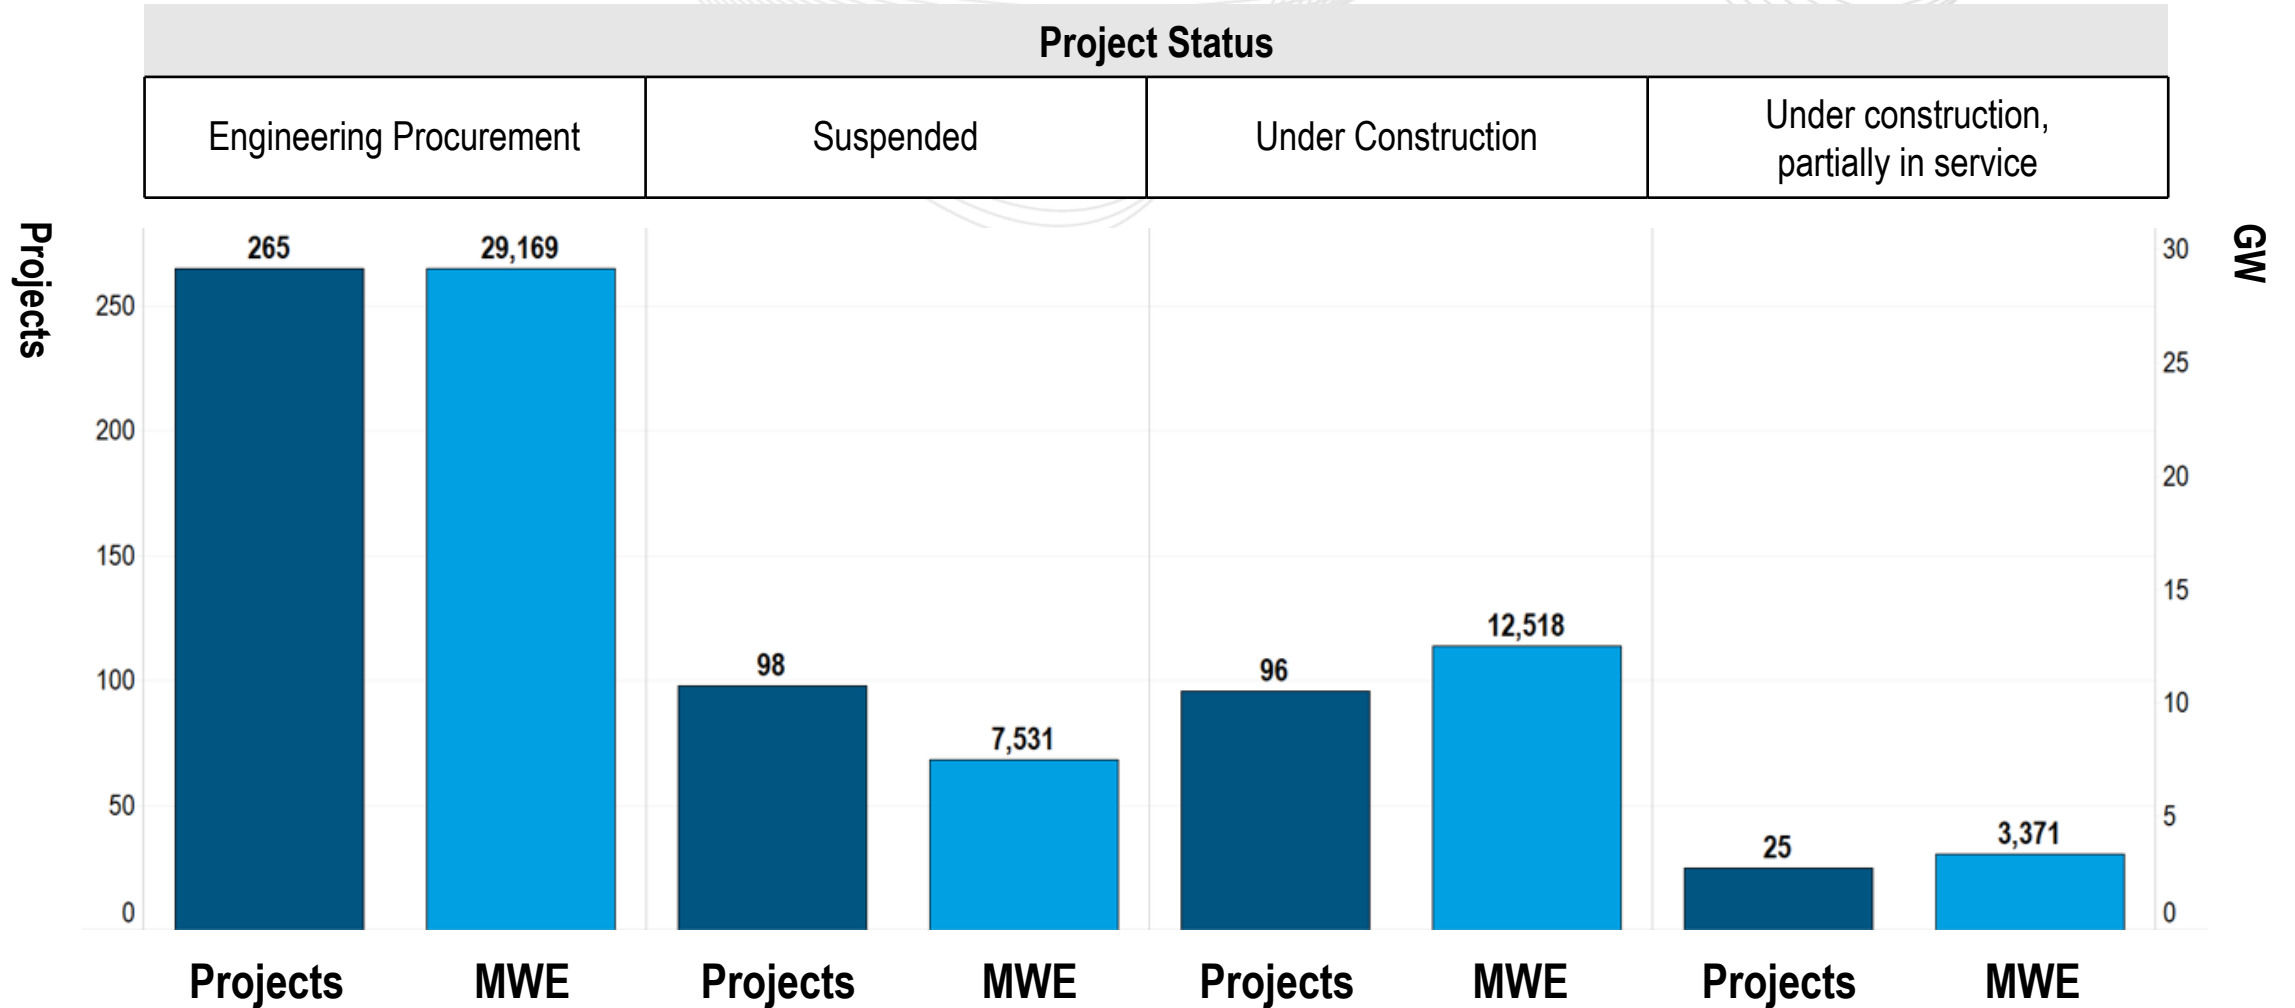

Withdrawn Projects by Year

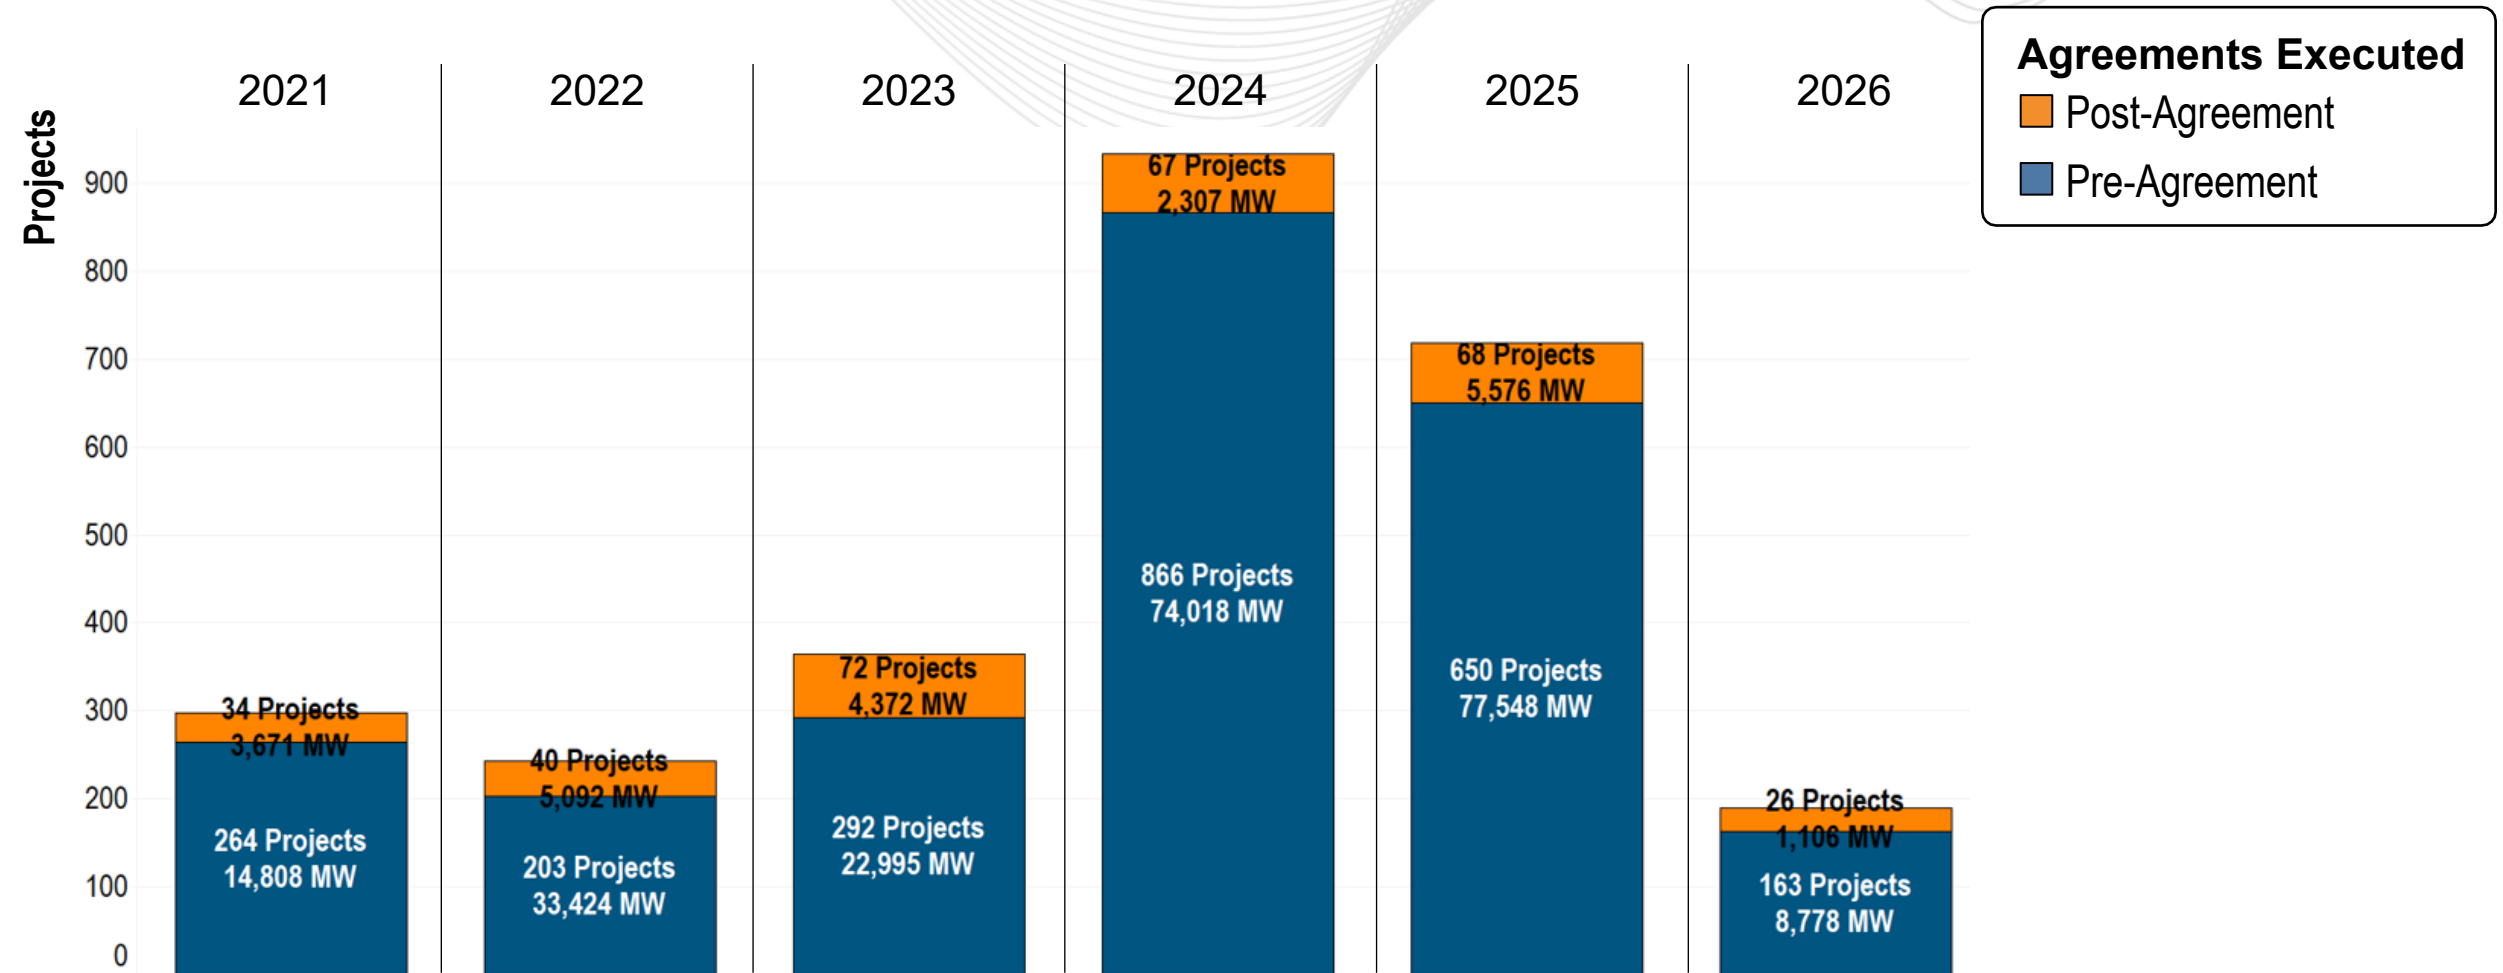

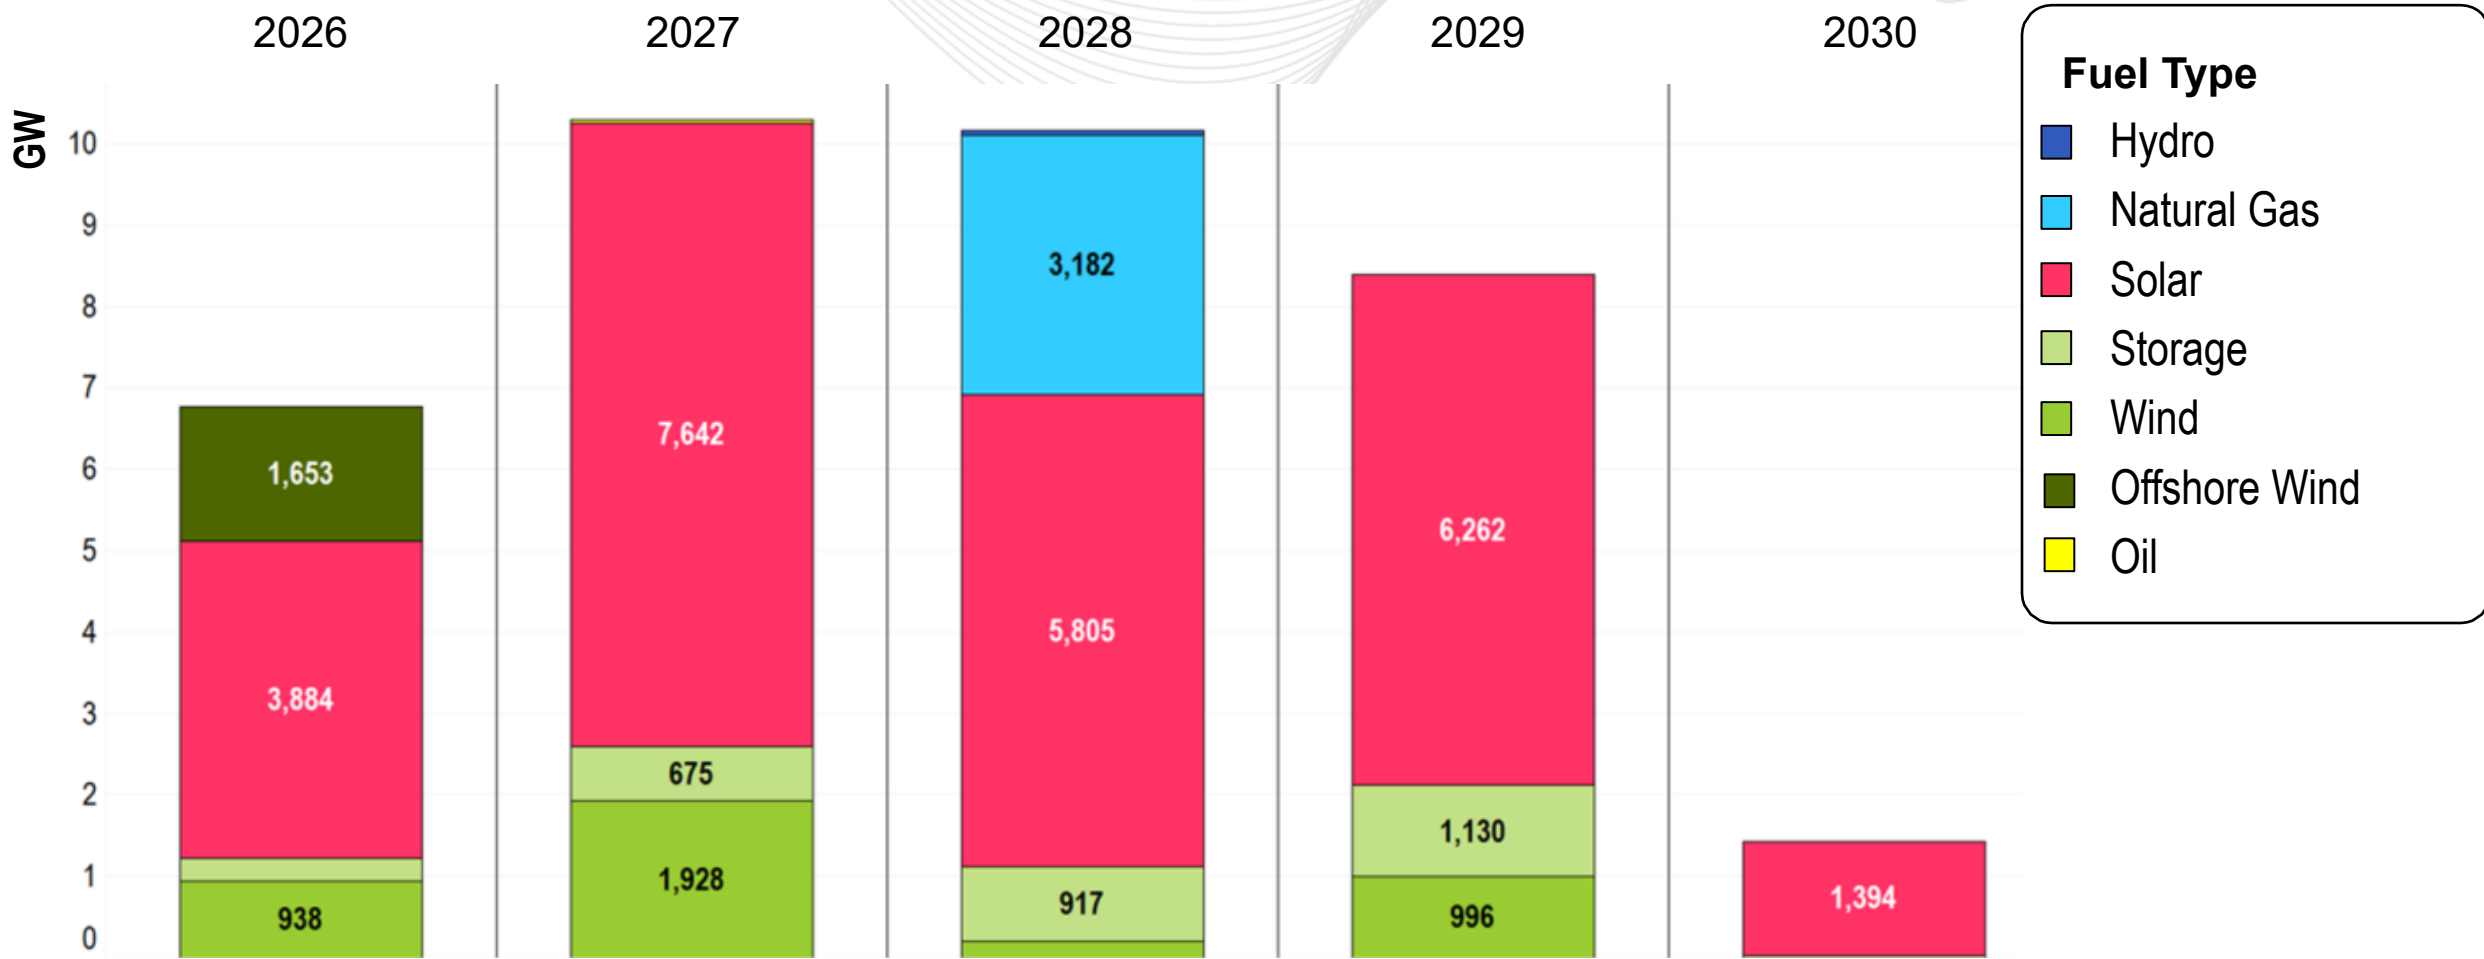

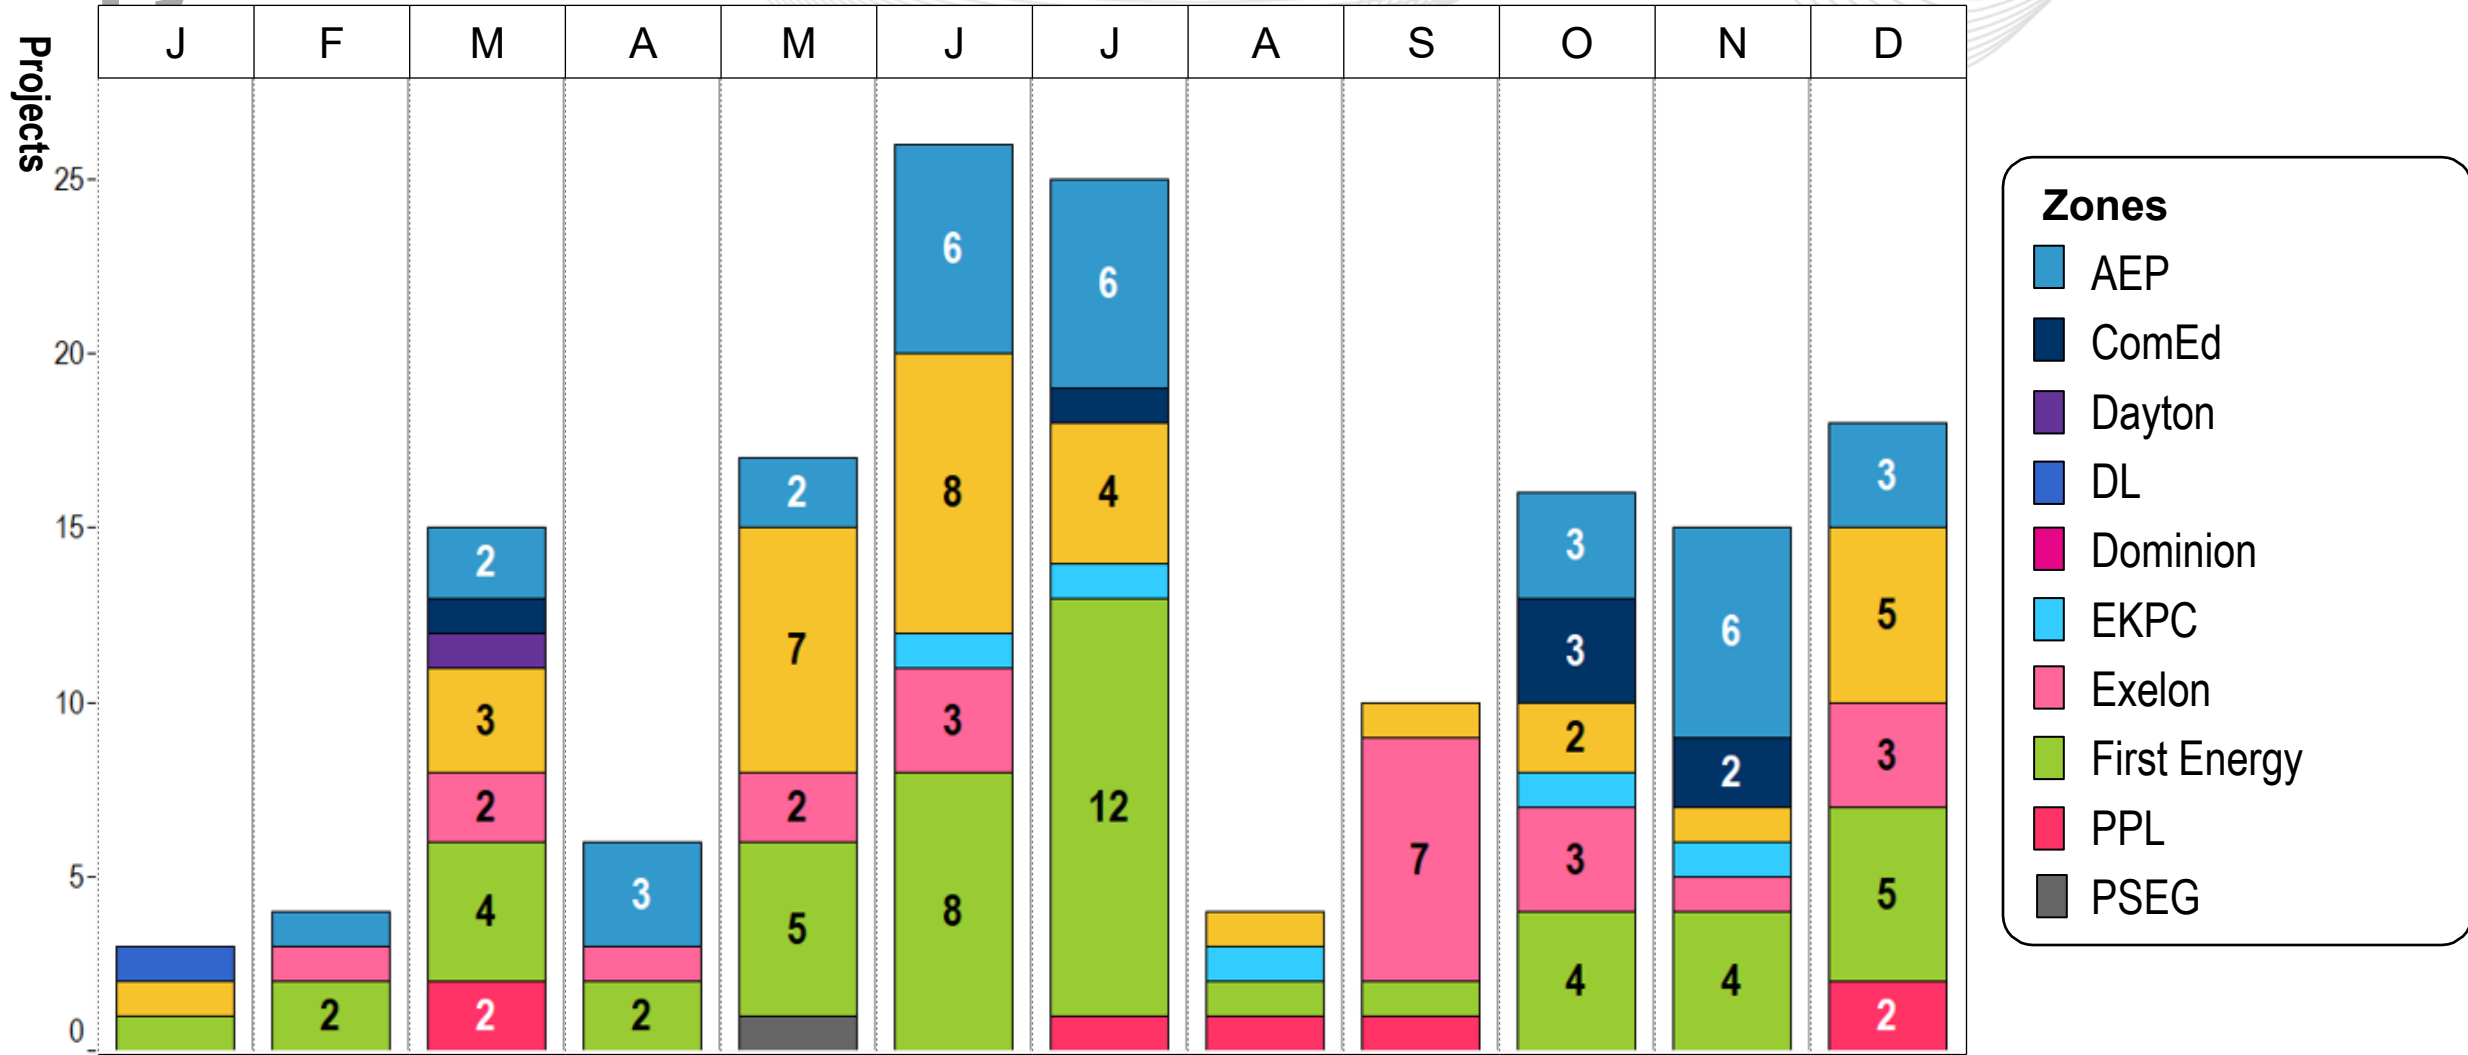

- Construction Status Changes Since January
 - 9,768 MWs have been withdrawn. 990MWs of which were in the construction phase.
 - 413 additional MWs have been placed in service.
 - 3,774 more MWs transitioned from Engineering Procurement to Under Construction.
 - Approximately 35% of the test energy dates in the last quarter moved

Presenter:

Nora Embert

Interconnection Construction
Management

Nora.Embert@PJM.com



Member Hotline

(610) 666 – 8980

(866) 400 – 8980

custsvc@pjm.com
