


AC² Go-Live Summary

November Committee Meetings

- What was the AC2 Project:
 - ✓ It was the largest and most complex PJM project
 - ✓ Five + years of design, development and testing
 - ✓ Dual Primary Control Centers
 - ✓ Separate and redundant EMS systems
- Months of Migration Planning:
 - ✓ Over 20 separate table top/mock migration exercises focusing on migration and back-out activities
 - ✓ 37 separate migration plans
 - ✓ Over 1500 separate individual migration tasks
- AC2 Migration Planning Status updates at multiple Committee meetings from May through November

Activity Ends (first hour is 11/07/11 18)

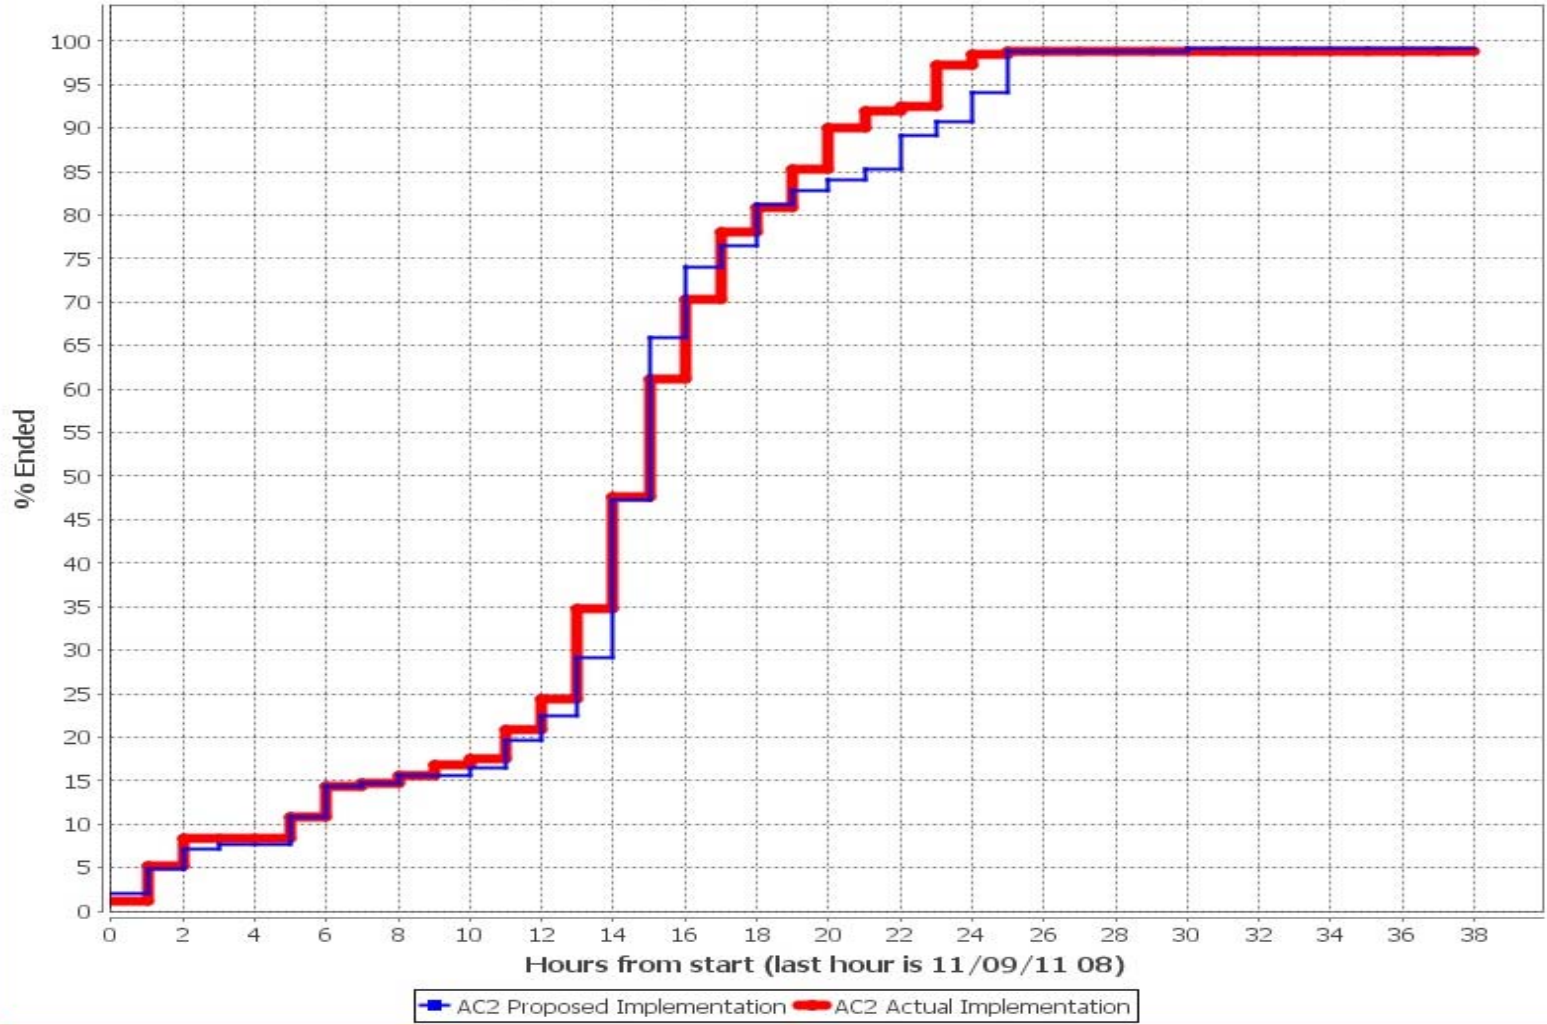

Milestones

Name	Est. Start	Est. End	Act. Start	Act. End
C1 BidPrd – AC2 BidPrd Propagation	11/07/2011 20:01	11/08/2011 05:00	11/08/2011 11:21	11/08/2011 04:25
ICCP Links	11/08/2011 08:30	11/08/2011 09:00	11/08/2011 08:57	11/08/2011 09:08
ICCP Links	11/08/2011 09:00	11/08/2011 09:30	11/08/2011 09:12	11/08/2011 09:56
Redundancy Checks	11/08/2011 09:30	11/08/2011 10:30	11/08/2011 09:57	11/08/2011 11:07

Application Outages

Name	Est. Start	Est. End	Act. Start	Act. End
eMarket	11/07/2011 20:01	11/08/2011 05:00	11/08/2011 11:21	11/08/2011 17:02
eDART	11/08/2011 06:31	11/08/2011 19:00	11/08/2011 06:30	11/08/2011 17:36
GPM	11/08/2011 07:01	11/09/2011 16:00	11/08/2011 07:01	11/09/2011 15:37
LRS	11/08/2011 07:01	11/08/2011 16:30	11/08/2011 07:02	11/08/2011 14:12
OASISWeb - Dispatch Rate Page	11/08/2011 07:01	11/08/2011 12:00	11/08/2011 07:46	11/08/2011 13:20
PJM.COM - MISO-PJM JCM Charts and Graphs	11/08/2011 07:01	11/08/2011 19:00	11/08/2011 07:46	11/08/2011 13:20
PJM.COM - Real-Time Statistics	11/08/2011 07:01	11/08/2011 19:00	11/08/2011 07:46	11/08/2011 13:20
eData	11/08/2011 07:01	11/08/2011 19:00	11/08/2011 07:46	11/08/2011 12:56
eDataFeed	11/08/2011 07:01	11/08/2011 19:00	11/08/2011 07:45	11/08/2011 12:58
OASISWeb - Operational Data Page	11/08/2011 08:31	11/08/2011 12:00	11/08/2011 08:55	11/08/2011 15:57
PJM.COM - Operational Data Page	11/08/2011 08:31	11/08/2011 12:00	11/08/2011 08:55	11/08/2011 14:31

- **Issues:**
 - eMkt access and database view issues.
 - AC2 Economic Max = 0 issue delayed Group A link implementation by 15 minutes.
- **Observations:**
 - Excellent coordination between PJM staff, PJM members and neighboring systems.
 - PJM members were extremely understanding and helpful in identifying and resolving data issues



Contact: Dave Souder
souder@pjm.com
610-666-4795
