Planning Parameter Deadline Reform

Andrew Gledhill
Resource Adequacy Planning

Markets & Reliability Committee
August 19, 2026

Disclaimer: While materials are current at the time of publishing, applicable requirements may change. PJM Governing Documents control.

PJM © 2026

Acronyms

ACRONYM	TERM & DEFINITION
IRM	Installed Reserve Margin
FPR	Forecast Pool Requirement (IRM converted to units of unforced capacity for use in the RPM auctions)
ELCC	Effective Load Carrying Capability
NOI	Notice of Intent
CETO	Capacity Emergency Transfer Objective
CETL	Capacity Emergency Transfer Limit
BRA	Base Residual Auction
IA	Incremental Auction

PJM © 2026

Pre ER24-99 RPM Planning Parameter Timeline

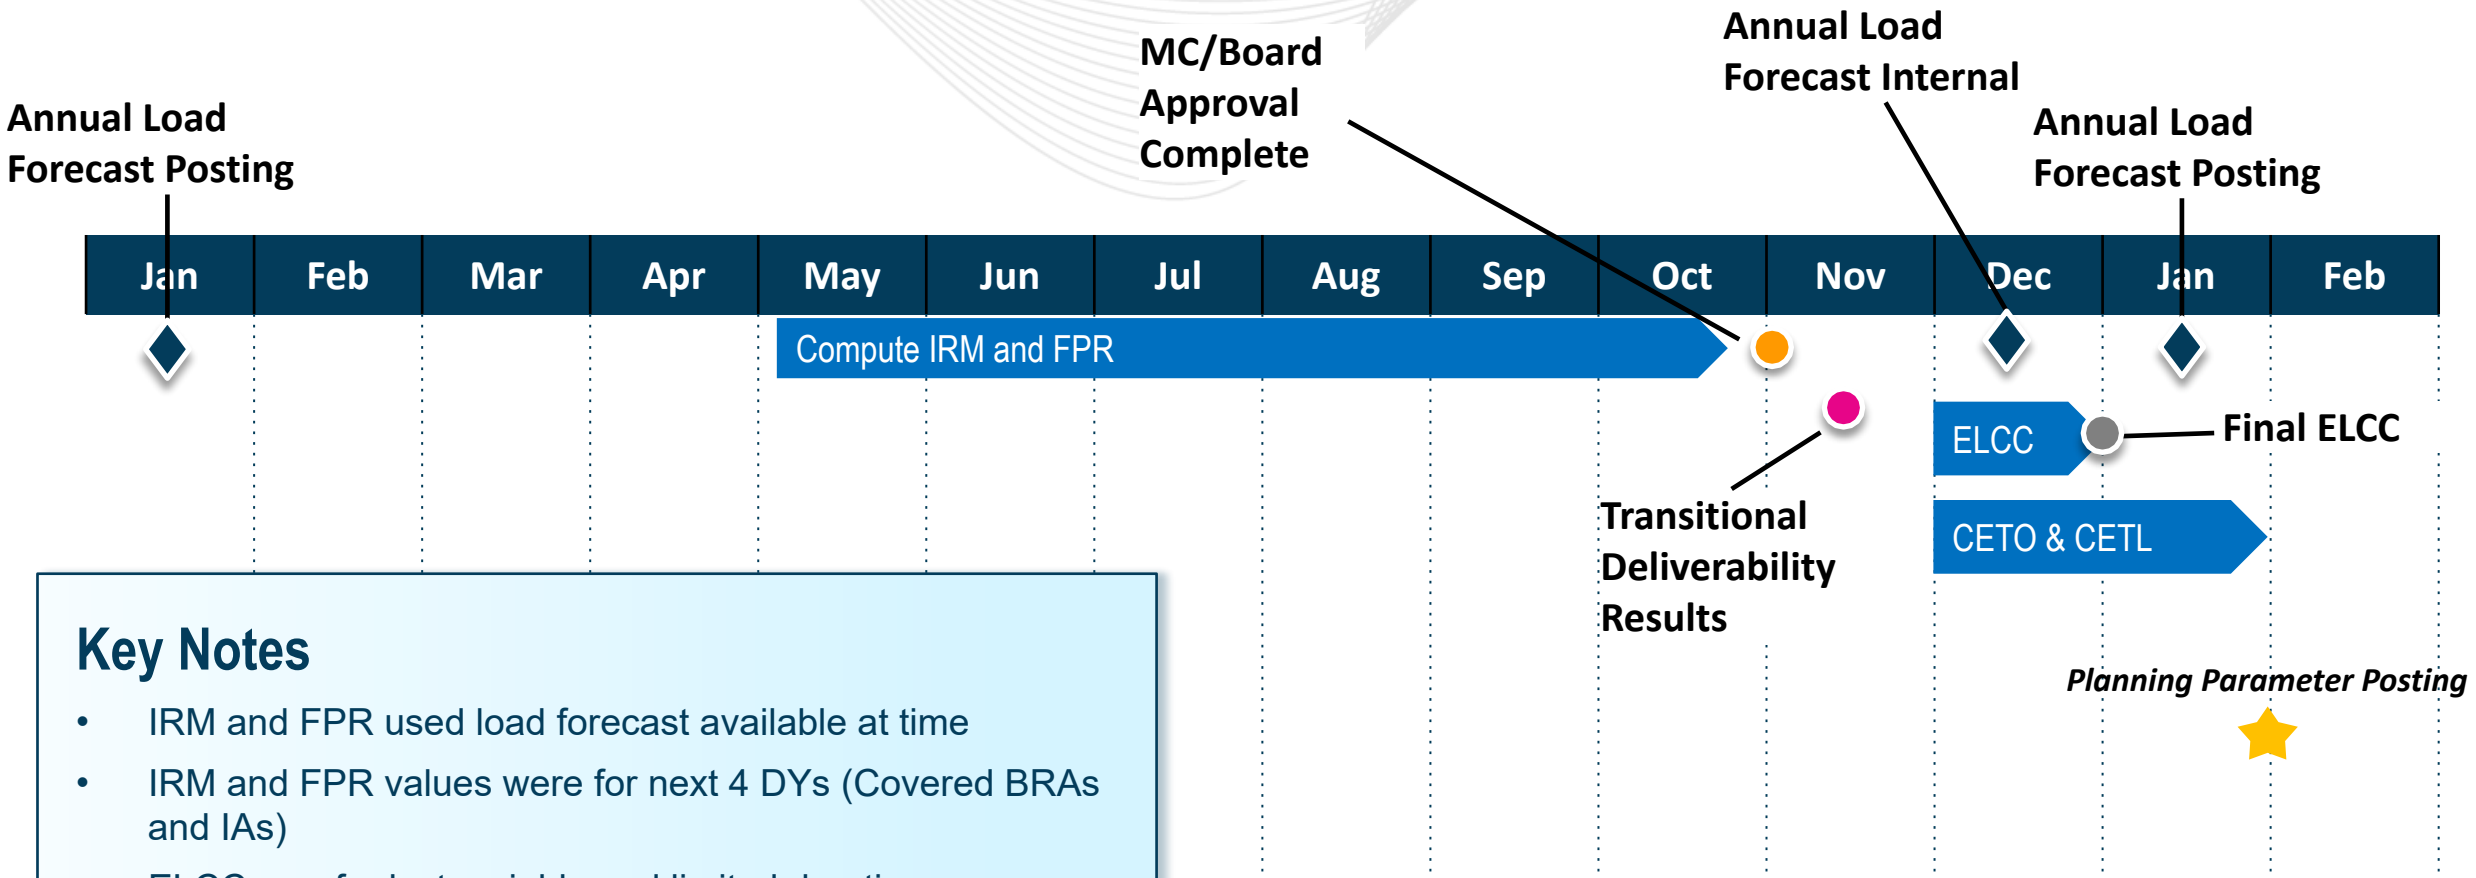

Key Notes

- IRM and FPR used load forecast available at time
- IRM and FPR values were for next 4 DYs (Covered BRAs and IAs)
- ELCC was for just variable and limited duration resources
- EFORd and ICAP/CIRs in IRM/FPR analysis were based on info available at time

PJM © 2026

Implied Post ER24-99 RPM Planning Parameter Timeline

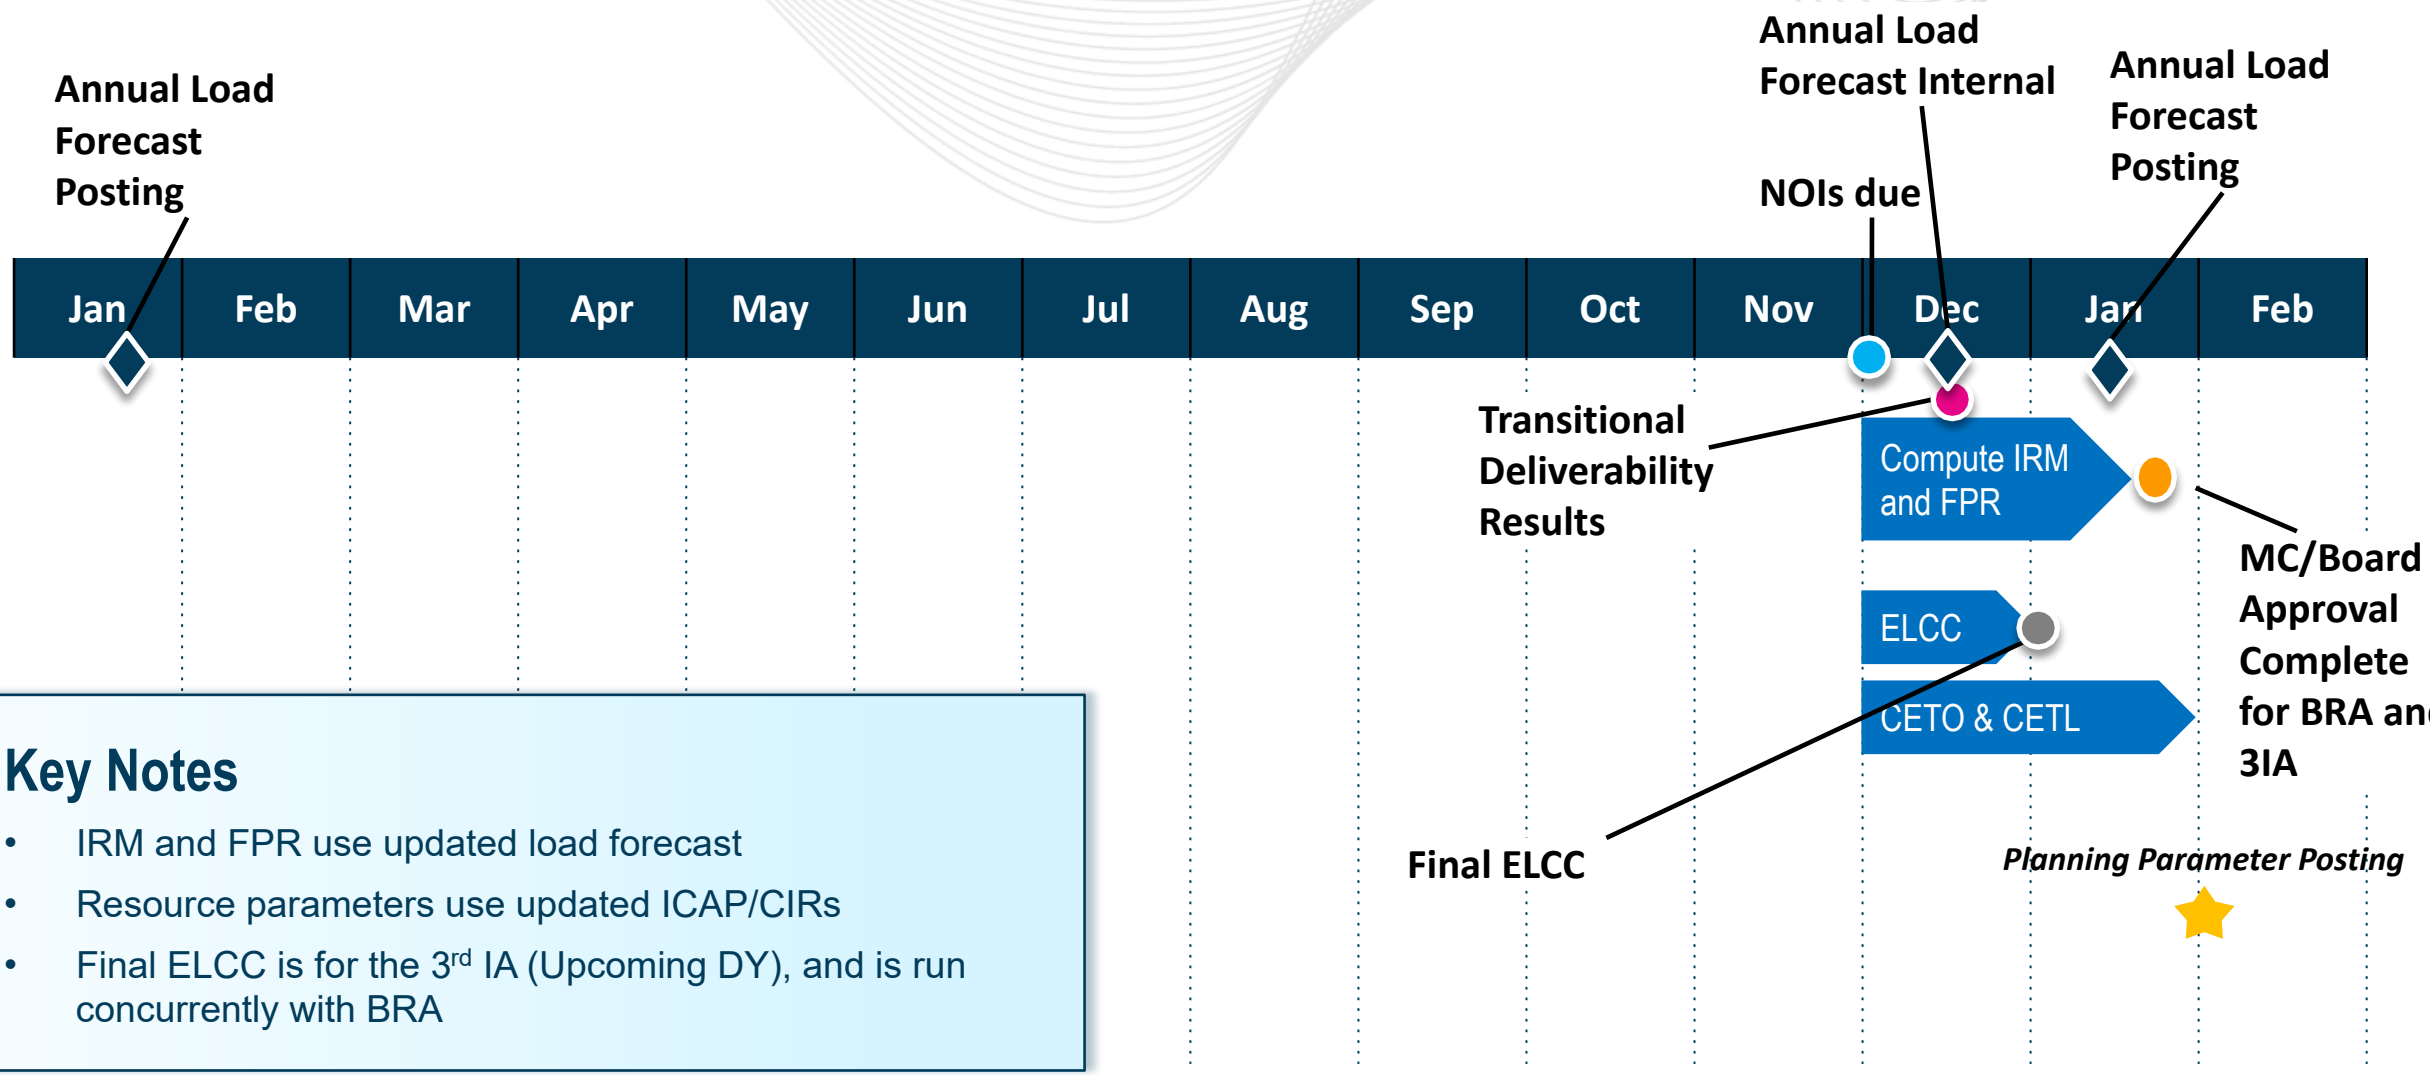

Key Notes

- IRM and FPR use updated load forecast
- Resource parameters use updated ICAP/CIRs
- Final ELCC is for the 3rd IA (Upcoming DY), and is run concurrently with BRA

PJM © 2026

Challenges with Implied Timeline

Planning Parameter deadlines are squeezed

- Analysis cannot begin until key data points are available
- Difficult to meet deadlines especially with adequate verification

Key Sequencing Events

FPR/IRM/ELCC analysis requires supply/demand data
Both are available mid-December

CETO analysis cannot begin until FPR/IRM/ELCC completes
Portfolio EUE is an input

CETL analysis cannot begin until CETOs are complete
CETOs are an input

PJM © 2026

Proposal

Problem

- There are approximately 9 weeks between when PJM Staff can start work and when the Planning Parameters are due.
- Staff requires approximately 12 weeks to complete.
- The sequencing and dependencies contribute to uncertainty on being able to meet deadline.

Solution

- Shift the BRA Planning Parameter due date from 2/1 to 3/1
- Shift the final ELCC values to be posted four months rather than five months prior to DY
- Shift 3rd IA Planning Parameter Posting deadline

PJM © 2026

Proposed Post ER24-99 RPM Planning Parameter Timeline

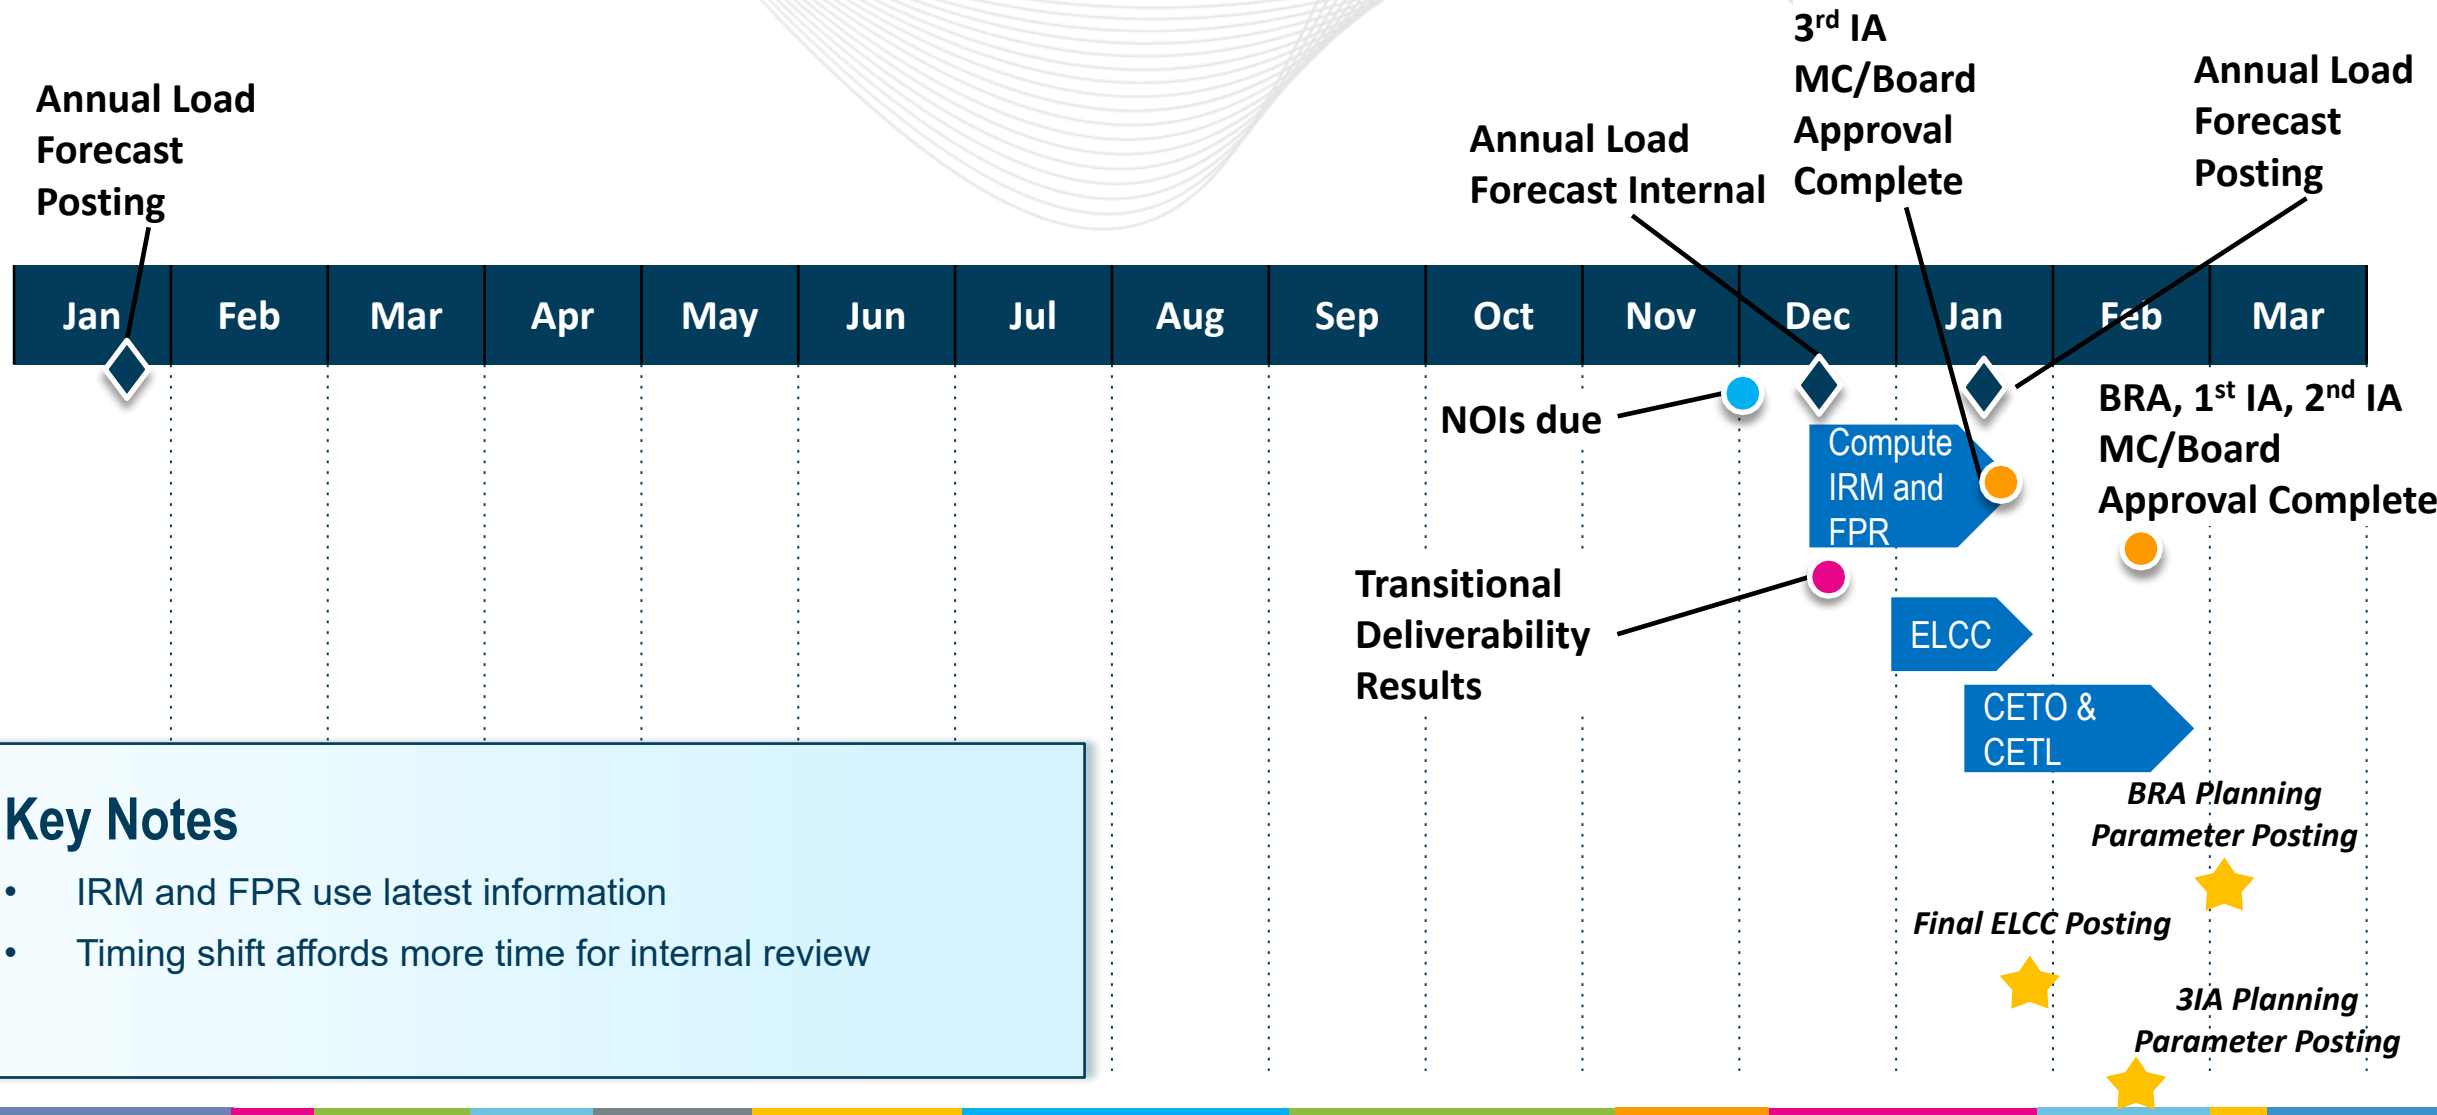

Key Notes

- IRM and FPR use latest information
- Timing shift affords more time for internal review

PJM © 2026

Proposed Post ER24-99 RPM Planning Parameter Timeline

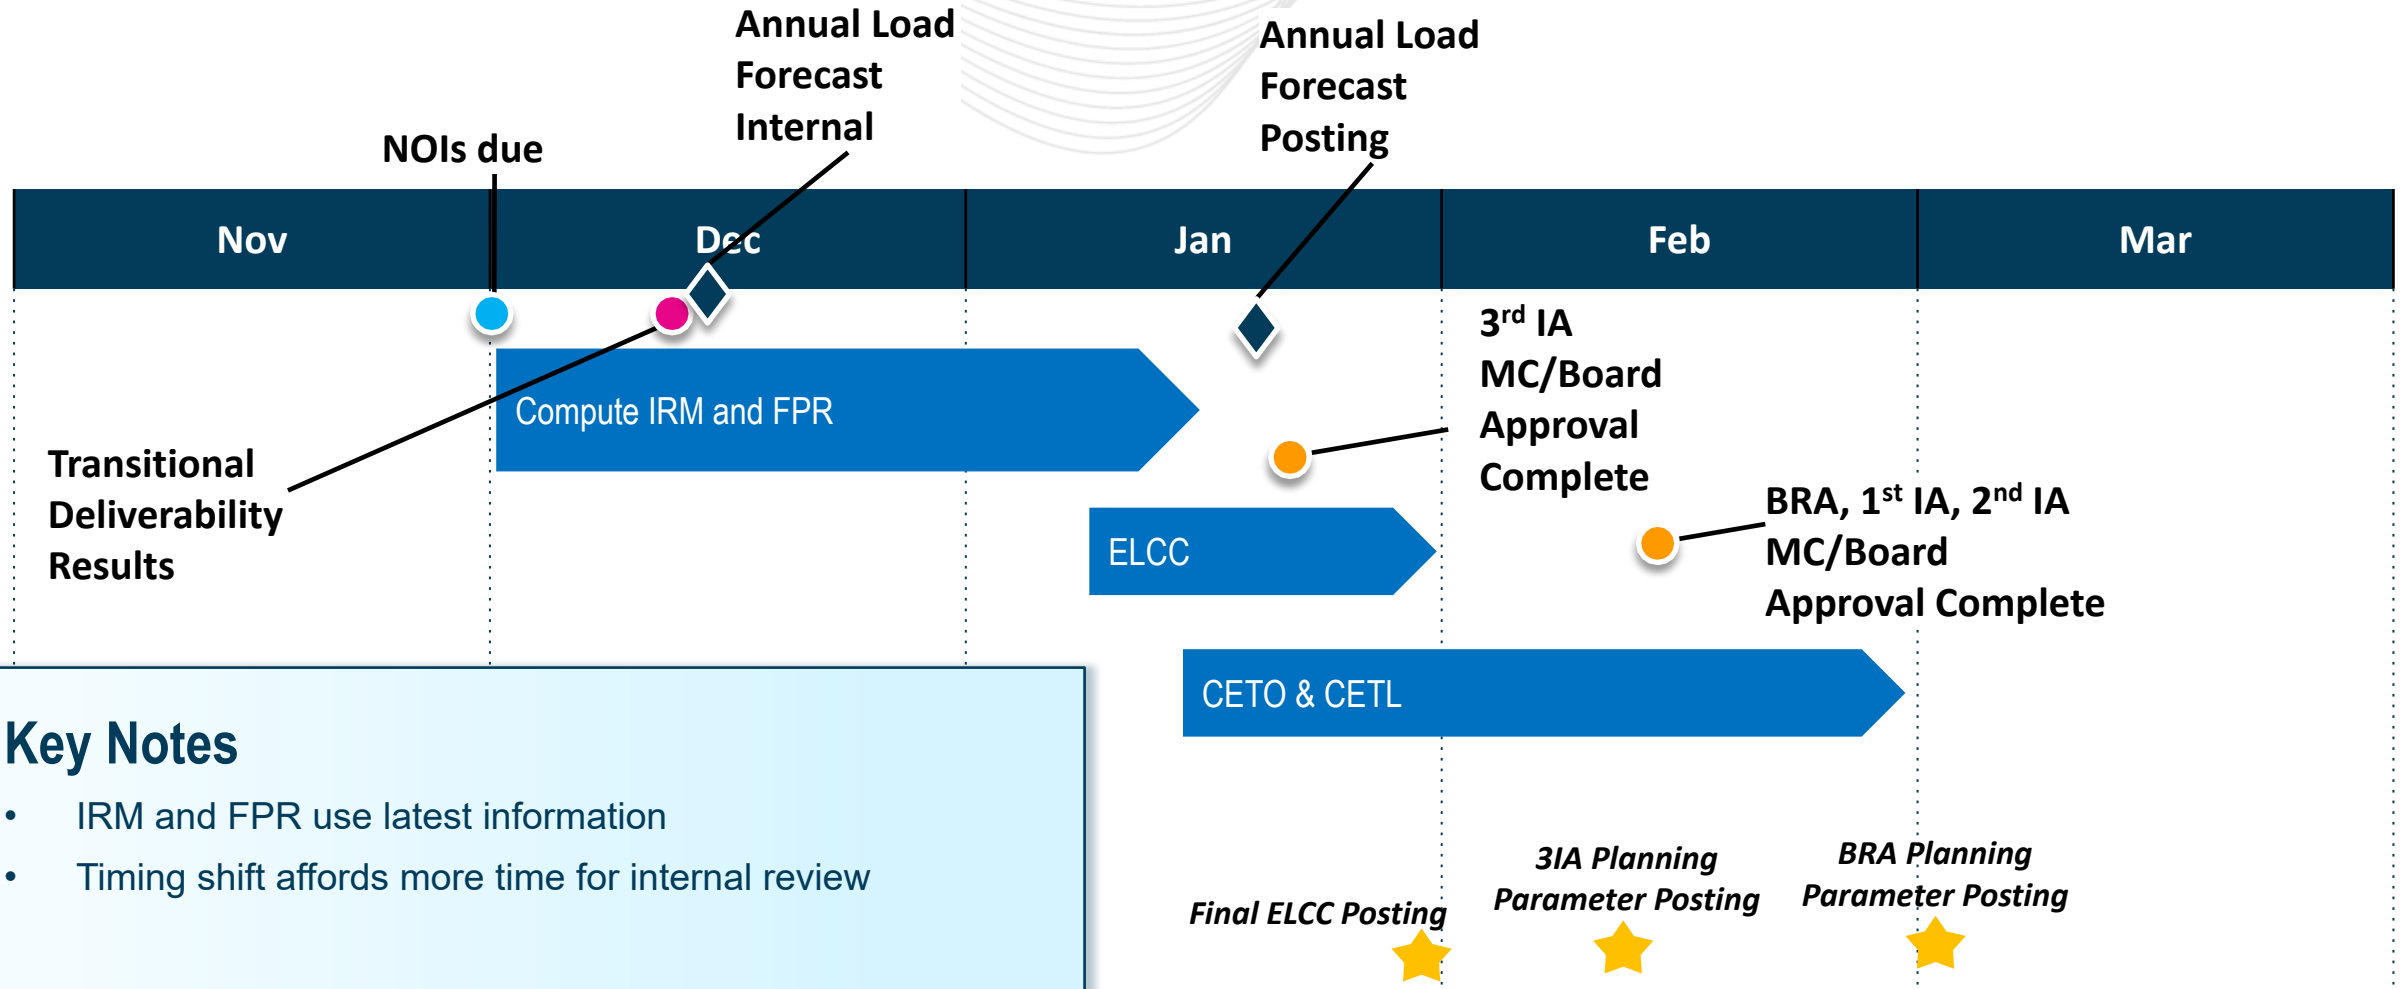

Key Notes

- IRM and FPR use latest information
- Timing shift affords more time for internal review

PJM © 2026

J. Administration of Effective Load Carrying Capability Analysis

The Office of the Interconnection shall post final ELCC Class Rating values at least once per year in a report that also includes appropriate details regarding methodology and inputs. The Office of the Interconnection shall post this report and shall communicate ELCC Resource Performance Adjustment values to applicable Capacity Resource Providers no later than ~~five~~four months prior to the start of the target Delivery Year, as described in the PJM Manuals. Accredited UCAP values for the applicable Delivery Year shall establish the maximum Unforced Capacity that an ELCC Resource can physically provide or offer to provide in the applicable Delivery Year.

PJM © 2026

Manual 18
5.2 RPM Auction Timeline

RPM Activity	TERM & DEFINITION
Post Planning Parameters for BRA	Posting deadline provided in RPM Auction Schedule on PJM website
Post RTO netCONE values for BRA	February 1
Post Final Planning Parameters for Third Incremental Auction	12 days ~~1 Month~~ prior to Third Incremental Auction
Final Accredited UCAP Factor for Delivery Year (effective with 2025/2026 Delivery Year)	No later than ~~5~~ 4 months prior to the start of the Delivery Year

PJM © 2026

5.10 Auction Clearing Requirements

a) vi) B)

The Office of the Interconnection shall determine the PJM Region Reliability Requirement and the Locational Deliverability Area Reliability Requirement for each Locational Deliverability Area for which a Variable Resource Requirement Curve has been established for such Base Residual Auction on or before ~~February~~ March 1, prior to the conduct of the Base Residual Auction for the first Delivery Year in which the new values will be applied, in accordance with the Reliability Assurance Agreement.

PJM © 2026

Review/Endorsement Timeline

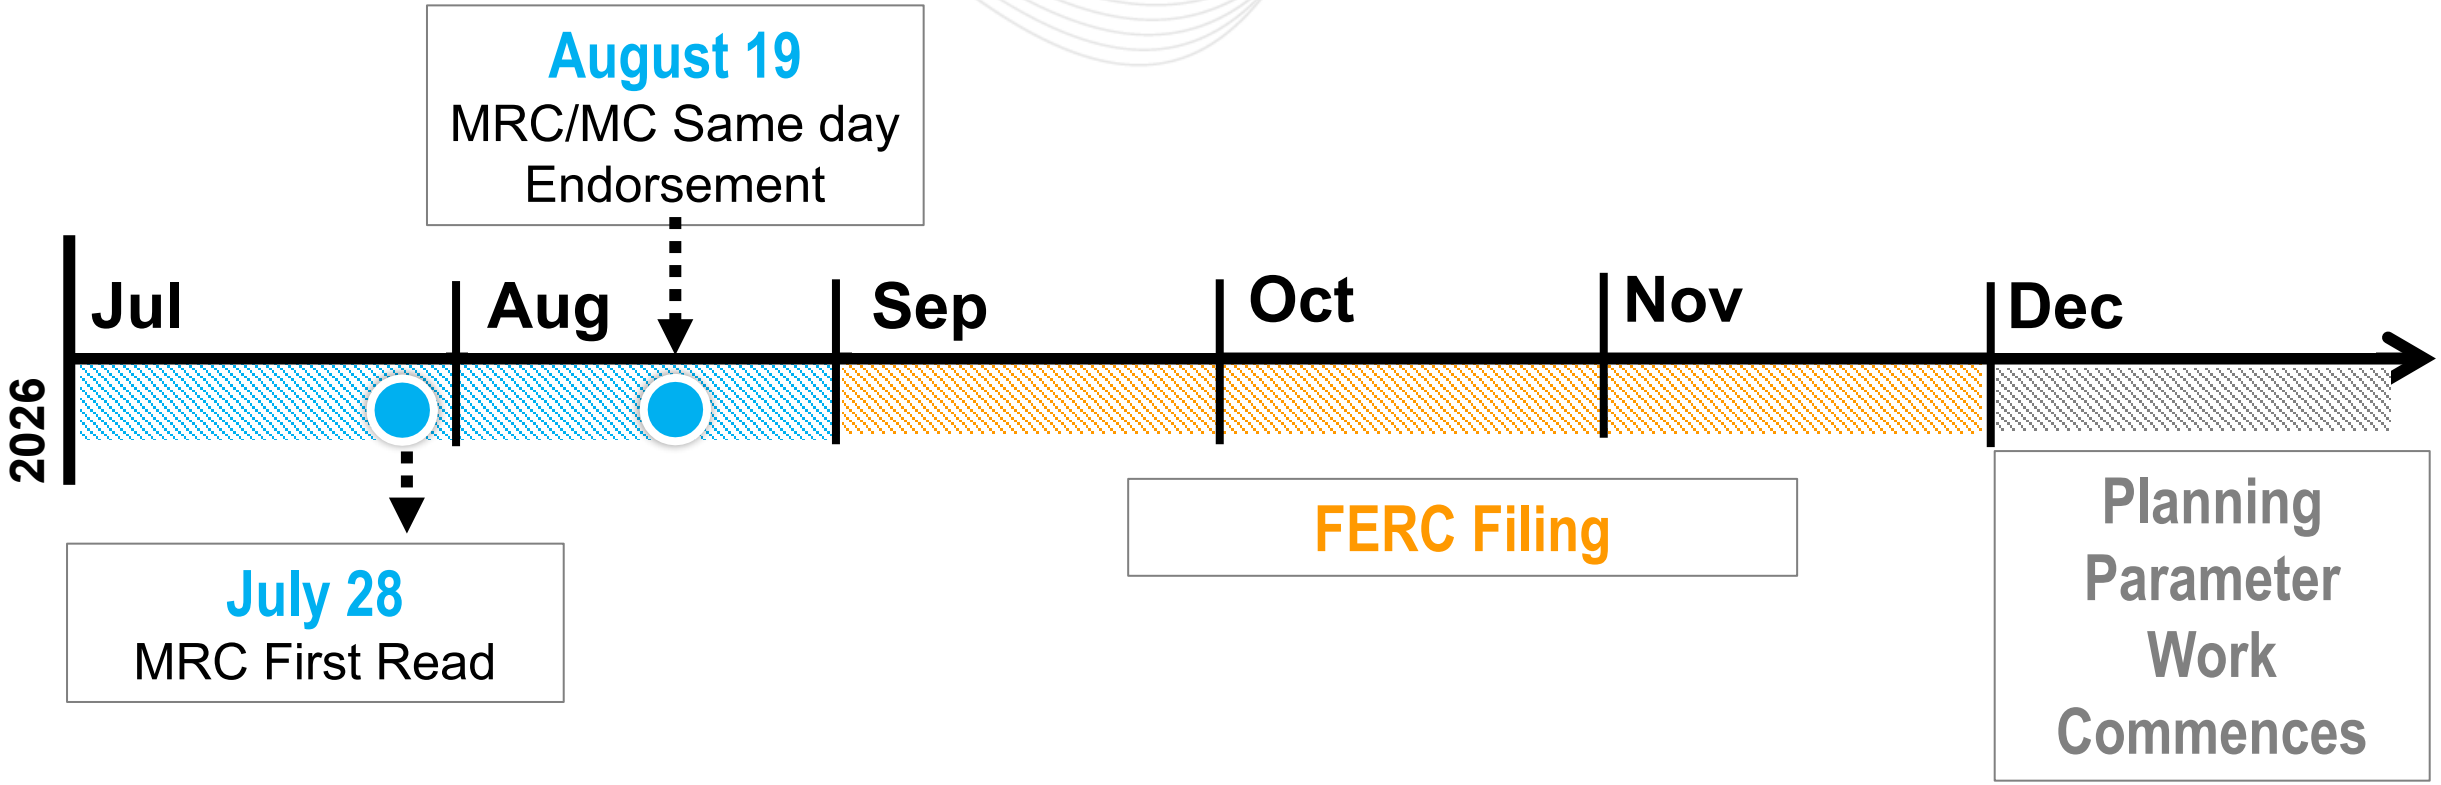

PJM © 2026

Potential Future Consideration

PJM is considering how best to solicit stakeholder and Board feedback

- Current process (RAA Schedule 4.B) solicits Members Committee recommendation and Board approval on the FPR and IRM. Members had previously expressed confusion around the purpose of the advisory vote.
- The current process could result in needing to recalculate the FPR and IRM, and finalization of the Planning Parameters beyond the posting deadline.
- PJM may bring an issue for future consideration.

PJM © 2026

Contact

Andrew Gledhill
andrew.gledhill@pjm.com

Planning Parameter Deadline Revisions

Member Hotline

(610) 666 – 8980

(866) 400 – 8980

custsvc@pjm.com

PJM © 2026

PROTECT THE POWER GRID

THINK BEFORE YOU CLICK!

pjm

BE ALERT TO MALICIOUS PHISHING EMAILS

Report suspicious email activity to PJM.

Call (610) 666-2244 or email it_ops_ctr_shift@pjm.com

PJM © 2026
